



**MHHS  
PROGRAMME**  
Industry-led, Elexon facilitated

---

# MHHS Change Control Webinar #3

## 26 June 2024

---

Version 1.0

MHHS-DEL2800


Document Classification: Public

# Agenda

#	Item	Objective	Lead	Time	Page
1	Welcome		MHHS PMO	13.30 - 13.35 5 mins	1
2	Presentation of CR051	Deferral of MHSSP-037	Tom Paterson, Elexon	13.35 – 13.50 15 mins	3
3	CR051 Q&A		All	13.50 - 14.00 10 mins	5

# Presentation of CR051

*Tom Paterson, Elexon*  
*15 mins*

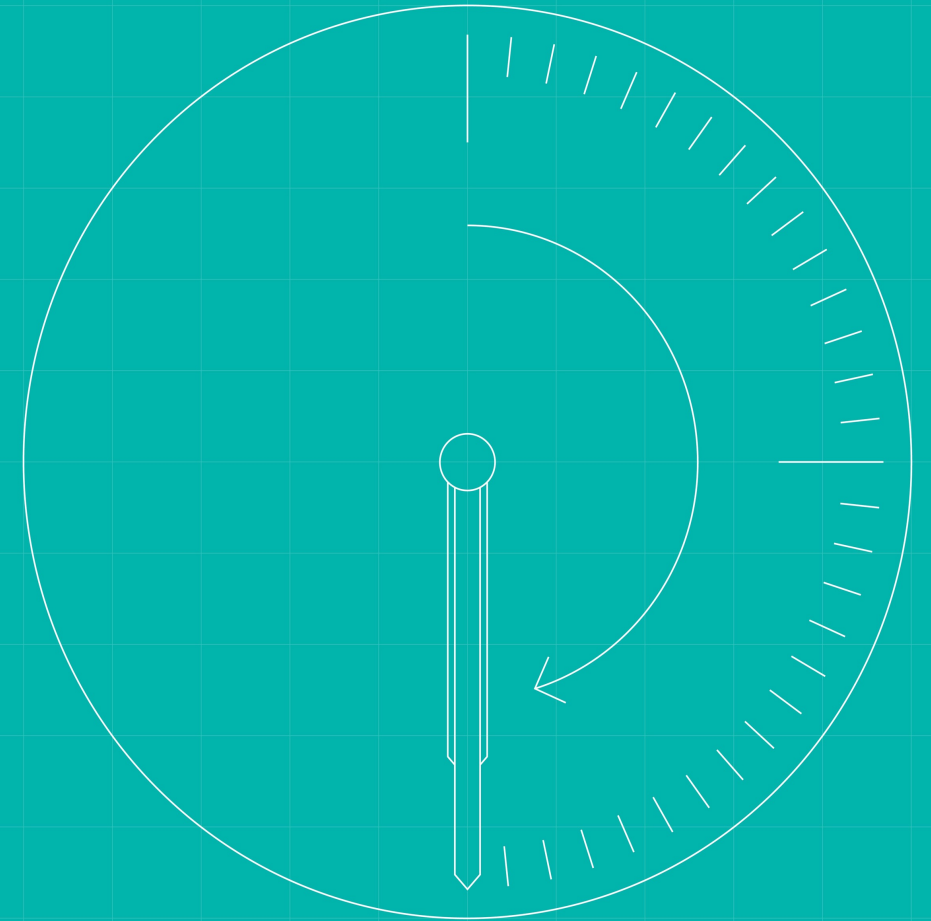

**Deferral of MHHSP-037**

**Issue Statement:**

- Business Requirement MHHSP-37 (i.e. LSS provides Load Shape data that is publicly accessible) is currently required to be delivered before M10. This will require ‘non-critical’ development work, putting unnecessary pressure on reaching M10, as Helix’s delivery capacity is already entirely directed towards meeting the ‘critical/must have’ requirements in support of MHHSP’s Industry Test Phases and key milestones (e.g. M10/M11).
- Delivering the Business Requirement after M10 would allow embracement of the opportunity to align the delivered solution against Elexon’s strategic platform (i.e. Insights) rather than the existing BSC website proposed when the requirement was originally written.

**Description of Change:**

- This CR requests a deferral, not a change, to the business requirement MHHSP-37 (i.e. LSS provides Load Shape data that is publicly accessible).
- It is proposed that the Business Requirement is delivered after M10, rather than before.
- Market Participants who require access to Load Shape Data will have gone through qualification, and would still be able to access this information via the associated IF flow(s).
- It is proposed that Business Requirement MHHSP-37 will instead be implemented at M11 + 6 months.\*

**Target Date of Change and Next Steps:**

- Following this industry webinar, the Change Request will be issued to IA. The results of the IA will be reviewed by Ofgem who approve or reject the continuation of the new process.

*\*this is a proposed, indicative date, and not a committed date by the Change Raiser until the Impact Assessment is complete and a decision is made.*

**Change Request Form**

**Change Request details**

Change Request Title	Deferral of MHHSP-037	
Change Request Number	CR051	
Originating Advisory / Working Group	LDP Discussion Forum	
Risk/issue reference		
Change Raiser	Tom Paterson, Elexon	Date raised: 17/06/2024

*For further guidance on how to complete this document please see the supporting Change Request Form Guidance for Programme Participants. The guidance will support raising a change and responding to a change request via Impact Assessment. The Change Raiser should consider sharing the draft Change Request Form with impacted programme parties, prior to submission to PIMO. The guidance, as well as other key documents are referenced below and can be found via the MHHS website.*


**Change Request to be read in conjunction with:**

- MHHS Change Request Form Guidance for Programme Participants
- MHHS Change Control Approach
- MHHS Governance Framework
- Ofgem’s MHHS Transition Timetable

**MHHS-DEL2785 CR051 Draft**

# CR051 Q&A

*All  
10 mins*

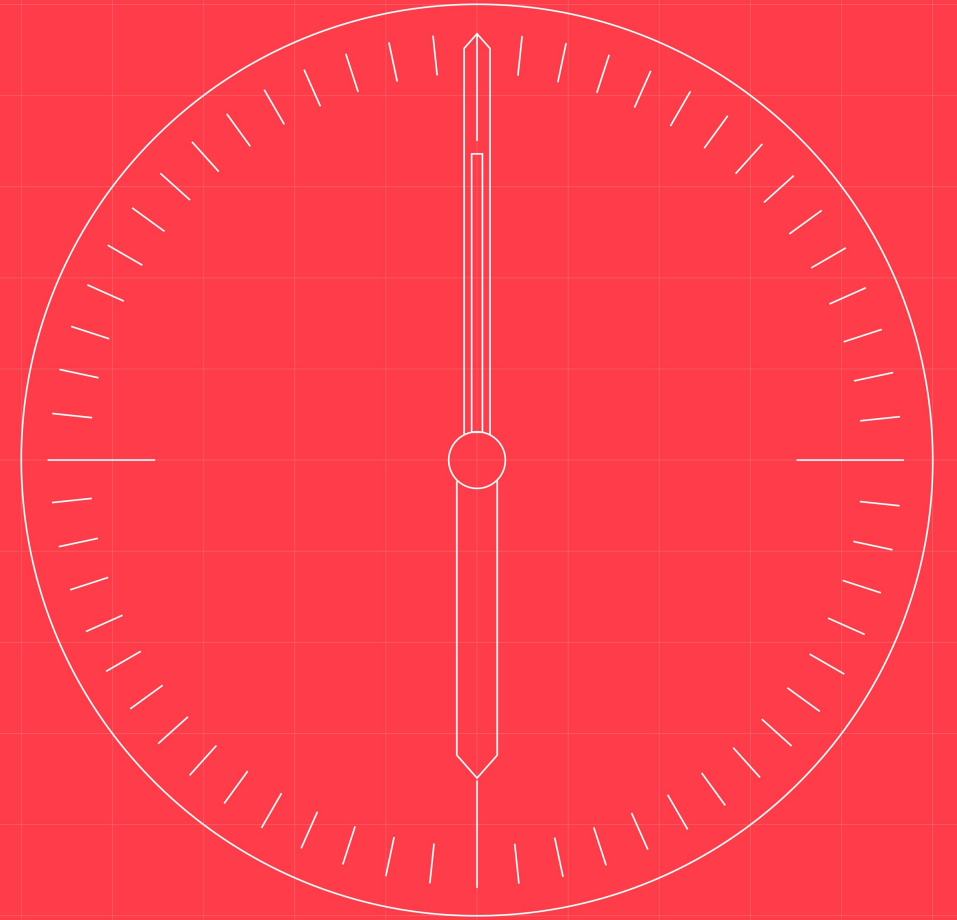

## Contact

PMO@MHHSProgramme.co.uk

# Thank you
