



**MHHS
PROGRAMME**
Industry-led, Elexon facilitated

Migration and Cutover Advisory Group (MCAG) #14 – 24 June 2025

Version 1.0

MHHS-DEL3858

Agenda


#	Item	Objective	Type	Lead	Time	Page
1	Welcome	Chair welcome	Information	Chair	14:00-14:05 5 mins	2
2	Headline Report and Actions	Approve headline report of previous meeting and review outstanding actions	Decision	Chair and Secretariat	14:05-14:10 5 mins	3
3	Service Design Update	Elexon (Helix) to provide an update on the Service Design	Information	Helix SM Team (Mark Scott, Ian Giles)	14:10-14:25 15 mins	5
4	M10 Readiness	Status update on M10 Acceptance Criteria	Information	Programme (Lewis Hall)	14:25-14:40 15 mins	18
5	TORWG Updates	Provide updates on TORWG	Discussion	Programme (Matthew Breen)	14:45-14:50 5 mins	20
6	DCWG Updates	Provide updates on DCWG	Discussion	Programme (Matthew Breen)	14:50-14:55 5 mins	22
7	MWG Updates	Provide updates on MWG	Discussion	Programme (Justin Andrews)	14:55-15:00 5 mins	24
8	Programme Milestones related to MCAG	Overview of upcoming Programme Milestones related to MCAG and any milestone changes for approval	Information	Programme (PMO)	15:00-15:05 5 mins	27
9	Top Programme Risks related to MCAG	Overview of Programme Risks related to MCAG	Information	Programme (PMO)	15:05-15:10 5 mins	29
10	Programme Updates	Provide updates from L2/3 governance groups and wider Programme activity	Information	Programme (PMO)	15:10-15:10 0 mins	32
11	Summary and Next Steps	Summarise actions/decisions and look ahead to the next MCAG	Information	Chair and Secretariat	15:10-15:15 5 mins	36

Headline Report and Actions

DECISION: Approve headline report of previous meeting and review outstanding actions

Chair and Secretariat

5 mins



Headline Report and Actions Review

- 1. Approval of Headline Report from MCAG held [27 May 2025](#).
- 2. **Review outstanding actions** (actions will be discussed by exception. Please review the action updates ahead of the meeting).


Ref	Action	Owner	Due	Latest Update
MCAG09-03	MCAG chair to review membership/attendees to ensure all dependencies are covered at MCAG.	MCAG Chair (Justin Andrews)	24/06/2025	ONGOING: Update to be provided at meeting.
MCAG12-01	The programme to log a risk/issue and produce clear guidance for Suppliers to engage with all agents and identify DCCs prior to migration.	Programme (Warren Fulton)	24/06/2025	RECOMMEND CLOSED: Item discussed in June 2025 MWG and position agreed. Guidance note added to MWG backlog, to be issued with other clarifications as we lead up to M10

Service Design Update

INFORMATION: Elexon (Helix) to provide an update on the Service Management Readiness

Helix SM Team (Mark Scott, Ian Giles)

15 mins



17 June, 2025

MCAG Update

- Service Management Readiness
– v1.0 (Final)
- Helix SM Team
 - Elexon



•01

Testing Update

- SIT Retest & ORT

SIT Retests

- SIT Retests started 9th June 2025
- Currently 8 SIT Retest have been completed:
 - Unscripted – Durabill - **Passed**
 - Unscripted – IF001 - **Passed**
 - Unscripted – Dead Letter - **Passed**
 - TC01 Retest – IMSERV raise P1 regarding HTTP error - **Passed**
 - Knowledge Article Upload – **Passed**
 - TC01 – Call to Service Desk – **Passed**
 - Change Email from DCC – **Passed**
 - Service Level Management Request – **Passed**
- SIT Testing completed 13th June 2025 with no new defects registered

- All preparatory work completed to start Operational Readiness Testing
 - ADO configured and accessible to ORT Participants and Testers
 - Test Cases uploaded to ADO
 - Communications Channel have been created.
 - ORT Test Briefings completed
 - Day in the Life (DITL) completed
- All ORT Test Dependencies have been completed – detailed below :
 - Cross - Party Service Desk Approach endorsed on the 19th May at e-TORWG – **Completed & Endorsed**
 - Cross - Party Service Desk Scenarios (Runbook) available from 30th May – **Completed & Shared**
 - Operations Manual (ORT Version) ready for TORWG on the 11th June (so will be shared on the 4th) – **Completed & Shared**
 - Service User LLSD (ORT Version) ready for TORWG on the 11th June (so will be shared on the 4th) – **Completed & Shared**
 - Test Scripts ready for eSITWG endorsement on the 10th June – **Completed & Endorsed**

•02

Elexon Upcoming Engagement Sessions

Elexon Upcoming Industry Engagement Sessions

Activity	Purpose	Audience	Date
Activity Operational Readiness Testing Participant / User Scheduling	Participants who have completed the form flagged earlier in the pack will be contacted bi-laterally to schedule their participation	MHHS Participants	1st May – 16th May
Activity Publish CPSD Scenario runbook	we will publish the CPSD Scenarios in a runbook (excel format) to the collaboration base with a form for requesting changes / adding scenarios	All MHHS Stakeholders	30 th May
Governance ORT Test Scripts updates walkthrough	Endorsement of test scripts for ORT	eSITWG	10th June
Activity Operational Readiness Testing	Execution of the agreed testing approach and scripts to identify any issues with intended CPSD operation.	MHHS Participants	16th June – 11th July
Activity Readiness workshops	To provide information that will support participants in creating and tracking support requests and incidents and conducting Self service triage.	MHHS Participants	1. 11th June 2. 26th June 3. 9th July 4. 24th July

•03

Updated Operations Manual & LLSD

- The updated Operations Manual (v1.4) has now been published (Wednesday 4th June) and incorporates recent feedback and comments we've received since v1.3
- We will continue to amend and update as further feedback is received, and any future versions will be published (monthly) ahead of each TORWG
- The sheet for recording further comments has been uploaded to the Collaboration Base to allow for ongoing, continuous feedback ([Operations Manual Feedback Spreadsheet](#))
- Version 2.0 to be published following ORT

- The updated Low Level Service Design (v1.2) has now been published (Wednesday 4th June) and incorporates recent feedback and comments we've received
- Version 2.0 to be published following ORT

•04

Useful Links

- Information Gathering Form

- <https://forms.office.com/e/tEMdp9EVgF>


Thank you

M10 Readiness

INFORMATION: Status update on M10 Acceptance Criteria

Programme (Lewis Hall)

15 mins

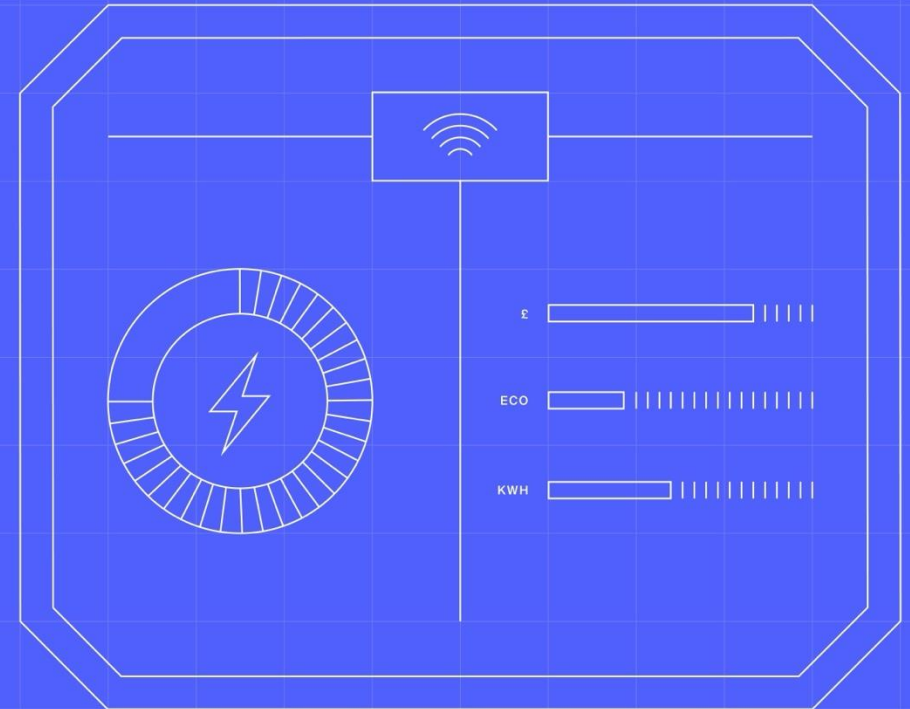


Content to be added by 20th June 2025

TORWG Updates

DISCUSSION: Provides updates on TORWG

Programme (Matthew Breen)

5 mins




- Over the past months, Central Parties, LDSOs and SIT Suppliers and Agents have been developing their own cutover plans and sharing them with the Programme
 - Central Parties submitted their Cutover Plans and completed templates by 16 May 2025 and the Programme shared initial feedback with each party, raising further questions or asking for more information based on the level of information that they have shared
 - LDSOs, SIT Suppliers and SIT Agents submitted their Cutover Plans and completed templates by 30 May 2025, the Programme is completing initial assurance of the submissions, and more detailed assurance will be carried out following the submission of updated / validated plans
 - The Programme are developing a consolidated Programme M10/M11 Cutover Plan which is due to be shared with Participants in June, there are some key updates required from Central Parties to feed into this version of the plan and meet these timelines
 - The Programme will be looking to schedule a Cutover walkthrough session with parties that are a part of the cutover to discuss a chronological run-through of the cutover activities, key learnings from the reviews, and dependencies between parties
 - Bilateral calls will be set up with Suppliers to discuss their cutover plans and the Agents that they are working with

DCWG Updates

DISCUSSION: Provides updates on DCWG

Programme (Matthew Breen)

5 mins

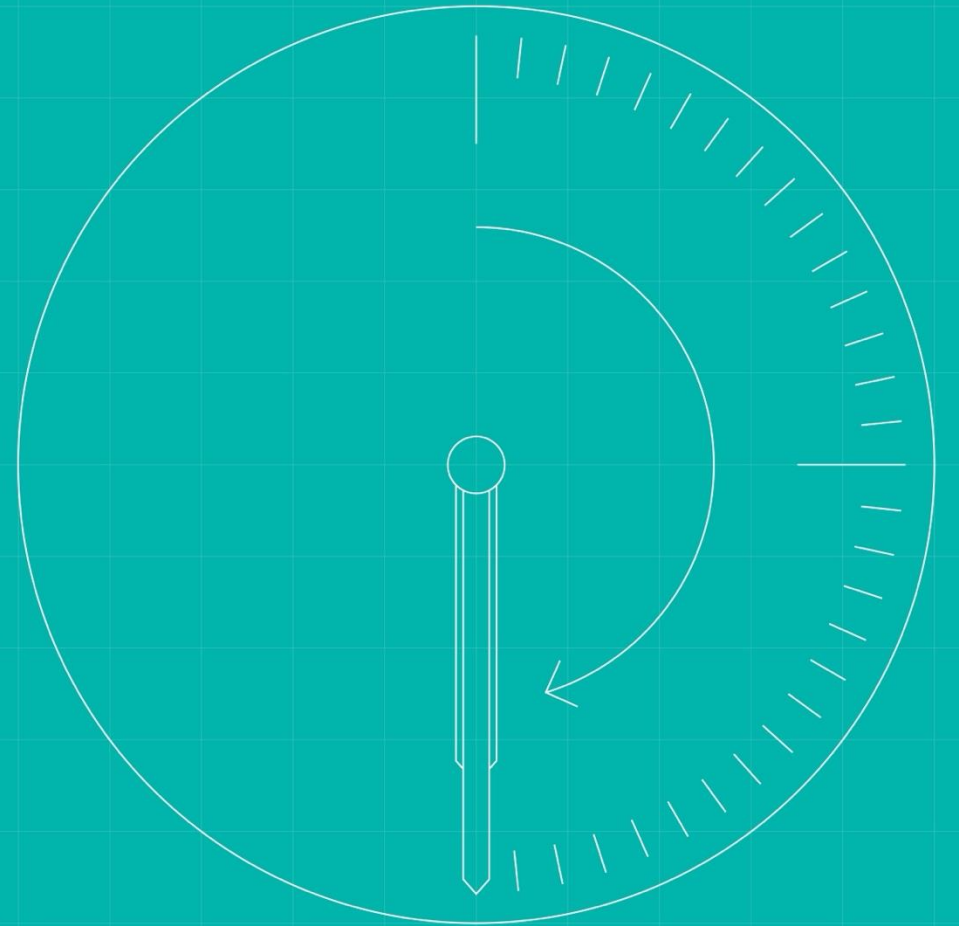

Updates from DCWG


- As per the updated Data Cleanse Plan v4.1, LDSOs, Suppliers and MEMs have been carrying out a series of activities related to connection type and meter type misalignments, linked import /export MPANs, and related MPANs
 - Participants have been sharing the volume of SDEP cases and exceptions as part of their self-declarations, the Programme continues to analyse responses against the EES report
 - Based on discussions at May's DCWG, a small date change will need to be made to the Data Cleanse Plan, relating to Traditional Meters installed on Current Transformers, to allow more time for Suppliers to fix these issues due to instances of Suppliers' MOPs not having the necessary information to make meter changes. The original date of 30 June 2025 has been extended to M11 and has been communicated to Suppliers
- Over the past few months, Suppliers have been investigating and resolving outstanding exceptions related to the population of ESME ID, Meter Location and Number of Displayed Register Digits, with deadlines on 16 May 2025 and 18 July 2025 for the completion of work-off plans
 - The Programme analysed responses from Suppliers regarding ESME ID and will provide a view of the next steps at June's DCWG
 - Based on figures shared by Suppliers in May, the current percentage of exceptions resolved for the population of Meter Location and Number of Displayed Register Digits is 79%
- The test process for the population of Domestic Premises Indicator will occur between 27 June – 11 July
 - LDSOs have confirmed to the Programme the individuals who require access to the SFTP environment to support this activity, and have now all been set up
 - The DCC has shared a sample extract with the Programme to help with the development of validation checks and to ensure the data items have been populated correctly

MWG Updates

DISCUSSION: Provides updates on MWG

Programme (Warren Fulton)

5 mins

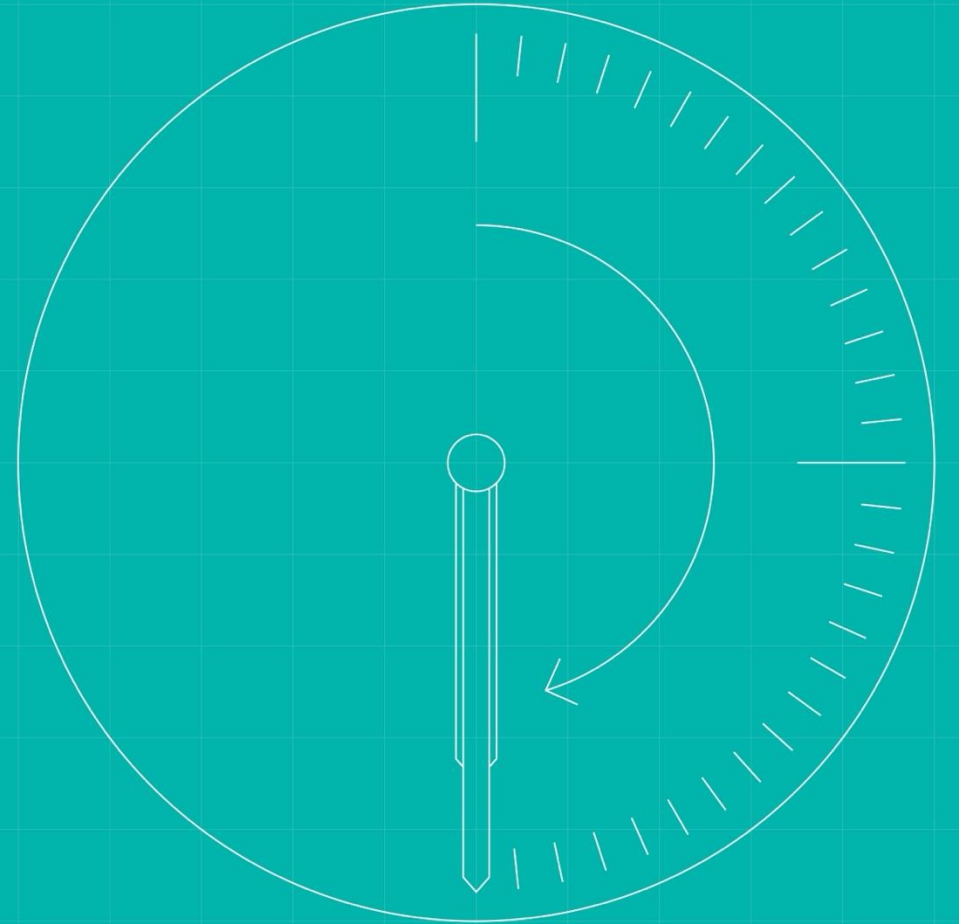

Migration Readiness Summary

Milestone Id	Milestone Name	Progress update	Target date	Status
Migration Framework				
T2-MI-7000	Framework Baselined at MCAG	At the April 2025 MCAG meeting, a unanimous decision was taken to baseline the Migration Framework	29/04/2025	Complete
Migration Schedule				
T3-MI-0043	Supplier Schedule Submission #2 complete	Schedule Submission 2 was initiated on 07 May 2025. Suppliers have until 20 June 2025 to submit their revised Migration Schedules.	20/06/2025	On track
T2-MI-7500	V1.0 of Migration Schedule Baseline approved at MCAG	Dependent on Supplier Schedule Submission 2	22/07/2025	On track
T2-MI-8000	Migration Sprint 0 schedule baselined (Sprint 0 commences at M11)	Sprint 0 planning is set to begin on 25-Sep-25	16/10/2025	On track

Migration Readiness Summary


Milestone Id	Milestone Name	Progress update	Target date	Status
MCC Mobilisation				
T3-MI-0044	MCC Dress Rehearsal 1 (To test the 'Initialise Schedule processes')	The dress rehearsal involving MCC and Suppliers is in progress.	15/07/2025	On track
T3-MI-0045	MCC Dress Rehearsal 2 (To test the 'Monitor and Control processes')	A second dress rehearsal involving MCC and all Programme Participants is scheduled to begin on 21-Jul-25 and remains on track	29/08/2025	On track
T2-MI-0500	MCC Mobilisation Complete	<p>MCC technology</p> <ul style="list-style-type: none">• Calculation engine and MCC Portal (Kestrel) went live on 7 May 2025• Reporting functionality is on track for Go-Live with Dress Rehearsal 2 <p>MCC resources</p> <ul style="list-style-type: none">• Recruitment activities completed and internal training has commenced <p>MCC processes and procedures</p> <ul style="list-style-type: none">• Development of Operational processes and Work Instructions is in progress.	29/08/2025	On track

Programme Milestones related to MCAG

INFORMATION: Overview of upcoming Programme Milestones related to MCAG and any milestone changes for approval

Programme (PMO)

5 mins



Look Ahead – Key Milestones Status at 19 May 25

To align to weekly reporting, the previous, current and forecast RAGs reflect milestone status from last week, this week and next week, respectively.


Milestone	Milestone Title	Forum	Baseline Date	Forecast Date	Responsible	Previous RAG	Current RAG	Forecast RAG	Commentary
T3-MI-0500	M16 methodology approved	MCAG (Transition)	26 November 2024	26 November 2024	SI Transition				25/03/25 - Transition Design (which underpins the M16 criteria) industry consultation, closed on 14/03/25. An internal working group between the Programme and BSCCo is drafting a response and looking agree the approach to defining the M16 criteria.
T3-MI-0043	Supplier Schedule Submission #2 complete	MCAG (Migration)	20 June 2025	20 June 2025	SI Migration				17/06/25 - 25% suppliers submitted, representing 1/3 MPANs, therefore there is a risk of all submissions not being sent by the milestone date. If a Participant does not submit a schedule or work off plan, this will be escalated to PSG and Ofgem.
T3-MI-0044	MCC Dress Rehearsal 1 - complete	MCAG (Migration)	15 July 2025	15 July 2025	SI Migration				17/06/25 - Activity on track.
T2-MI-7500	V1.0 of Migration Schedule Baseline Approved at MCAG	MCAG (Migration)	22 July 2025	22 July 2025	SI Migration				17/06/25 - Activity on track.
T2-MI-0450	Pre-migration data cleanse complete	MCAG (Transition)	13 August 2025	13 August 2025	SI Migration				17/06/25 - Activity on track.
T2-MI-0350	DCC Capacity Upgrade Operational	MCAG	29 August 2025	29 August 2025	PP				17/06/25 - Activity on track.
T2-MI-0500	MCC Operational Complete	MCAG (Migration)	29 August 2025	29 August 2025	SI Migration				17/06/25 - Activity on track.
T3-MI-0045	MCC Dress Rehearsal 2 - complete	MCAG (Migration)	29 August 2025	29 August 2025	SI Migration				17/06/25 - Activity on track.
T3-MI-0035	MCAG (Confirm that the Programme can Enter M10)	MCAG (Transition)	19 September 2025	19 September 2025	SI Migration				17/06/25 - Activity on track.
T3-MI-0034	Central Systems live and Codes designated at 00:00	MCAG (Transition)	22 September 2025	22 September 2025	SI Transition				17/06/25 - Activity on track.
T2-MI-8000	Migration Sprint 0 Schedule Baselined	MCAG (Migration)	16 October 2025	16 October 2025	SI Migration				17/06/25 - Activity on track.
T3-MI-0036	MCAG (Provide recommendation to PSG on M11 decision)	MCAG (Transition)	20 October 2025	20 October 2025	SI Migration				17/06/25 - Activity on track.
T2-MI-8500	Non-SIT Participants Migration Start	MCAG (Migration)	15 May 2026	15 May 2026	SI Migration				17/06/25 - Activity on track.
T2-MI-9000	Sprint Execution End	MCAG (Migration)	05 May 2027	05 May 2027	SI Migration				17/06/25 - Activity on track.

Top Programme Risks related to MCAG

INFORMATION: Update on the top Programme risks related to MCAG

Programme (PMO & Workstream Leads)

5 mins

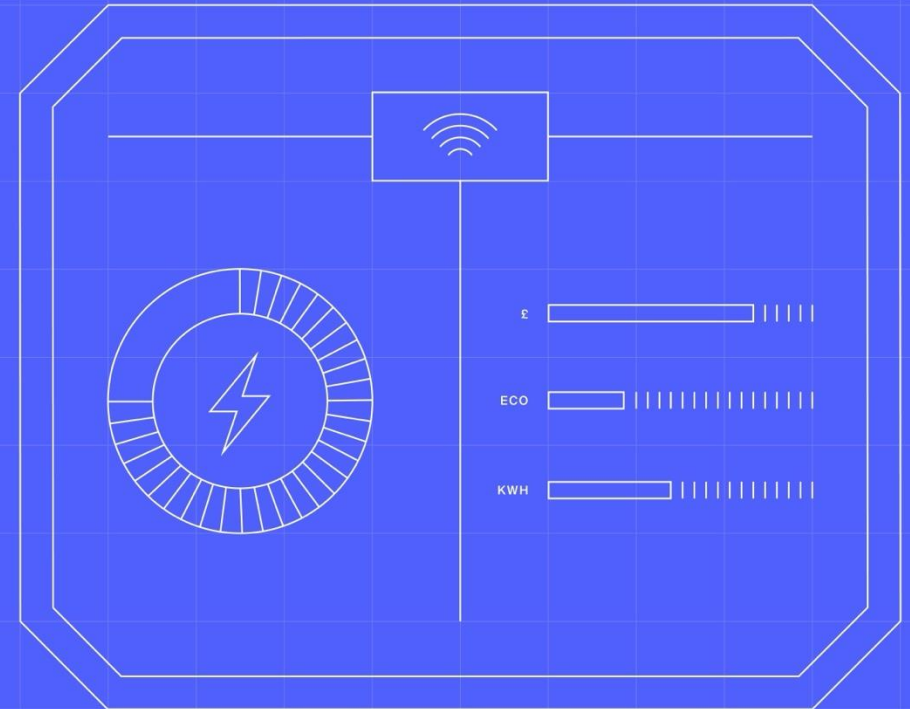

Theme		Summary						Mitigation Approach Overview																															
Commencing and completing Migration successfully		The theme explores the factors which may affect the Programme meeting M10 / M11 and completing Migration and how the Programme is planning to mitigate these to stop these risks from converting into issues						<ul style="list-style-type: none">Some of the existing risk factors around M10 / M11 will be mitigated by the findings throughout SIT Testing, which will evaluate assumptions, highlight to the Programme the areas which require attention and allow the Programme enough time to make the changes necessary for M10 / M11 successThe Migration Design, the Migration Cutover & Data Strategy, the Data Cleanse Plan, the Migration Thresholds Document and ongoing Code Drafting will provide Participants necessary materials to prepare for M10 / M11																															
Key Risks																																							
Risk ID	Risk Description	Risk Score Assessment																												Current score movement since last MWG	Mitigation Plan								
		Critical						High						Medium						Low																			
		30	29	28	27	26	25	24	23	22	21	20	19	18	17	16	15	14	13	12	11	10	9	8	7	6	5	4	3			2	1						
R663	There is a risk that those large Supplier Agents, who support multiple large Suppliers, will not be able to support planned migration volumes due to operational or technical constraints																	I	C	T												Score remains at 14	1. 17/02: Programme asking all SIT Suppliers to complete the proforma and return it to PPC@mhhsprogramme.co.uk no later than 17:00 on Monday 24 February 2025. 2. 19/03: No further updates. 3. 17/06: Risk to be assessed as part of Supplier Submission 2 which closes on 20/06						
R488	There is a risk that a significant volume of export MPANs created within Programme transition timescales will impact the ability of suppliers and DNOs to deliver Programme Migration																	I		C												Score remains at 13	1. 17/07: Awaiting formal position from Ofgem. 2. 04/12: Programme's working assumption is that Bulk creation of Export MPANs will not be undertaken until MHHS Migration is completed, however, should Suppliers plan to undertake bulk creation of Export MPANS, this needs to be included in Supplier Migration plan submissions. 3. 17/06: No further updates.						
R700	There is a risk that Suppliers and Agents do not complete Qualification in line with their delivery plans and this places pressure on the volumes that need to be delivered over the remainder of the migration period																	I		C												Score reduced from 17 to 12	1. 16/04: Lessons learnt exercises have taken places with LDSOs and SIT Parties to understand issues with process. Technical enhancements to QAD portal to support code body tracking of responses. Resource review taking place based on lessons learnt from initial QAD submissions. REC Implementing improved query management and process which will be rolled out to parties. As PPs have been through a cycle of QAD review, expectations of Code Bodies are clearer, so less work is anticipated at the second cycle of review. 2. 14/05: Testing and code reviews are currently on track, risk scoring lowered.						
		Key																																					
		I	Initial Score																																				
		C	Current Score																																				
		T	Target Score																																				


Key Risks																																	
Risk ID	Risk Description	Risk Score Assessment																												Current score movement since last MWG	Mitigation Plan		
		Critical						High						Medium						Low													
		30	29	28	27	26	25	24	23	22	21	20	19	18	17	16	15	14	13	12	11	10	9	8	7	6	5	4	3			2	1
R677	There is a risk that performance testing of the migration functionality within MPRS identifies an issue that cannot be resolved in time for SIT and non-SIT LDSO Non-Functional Testing. Risk is that LDSOs cannot meet migration thresholds. LDSOs need to carry out performance testing with their service providers i.e. SCS									I									C													Score remains at 12	1. 07/10: SIT and Non-SIT LDSO QT NF teams will share PIT evidence with MCC for them to carry out any additional assurance activity. As well as the requirement to for each LDSO to evidence that their PIT will meet Migration thresholds is set out in the PIT guidance. 2. 13/01: Programme are completing as much early testing as possible, and timelines have been reviewed by Ofgem and are realistic. 3. 17/04: Ongoing and continues to be monitored. 4. 27/05: SIT NF Testing execution is complete and with SRO for review
R828	There is a risk that Suppliers initiate more migrations than planned, or exceed the Threshold volumes																I		C													Score reduced from 18 to 12	1. 14/02: Exploring regulatory mechanisms that deal with scenarios where participants breach agreed system thresholds. 2. 19/09: Migration governance framework developed with MWG. Incentives to be developed with Code Bodies. 3. 04/12: Migration Governance Framework has defined governance processes, awaiting Ofgem CR055 directive outcomes. 4. 04/04: No further updates. 5. 06/05: The ELS model has been baselined which sets the overall number of migrations that can take place daily during each phase of ELS. The MCC will ensure that participants plan within these volumes. 6. 10/06: Migration team are working on the processes at the moment to deal with instances where Migrations exceed the Thresholds. The team plan to discuss these draft processes at the July MWG. Scoring reduced.

Programme Updates

INFORMATION: Provide an overview of activity at other MHHS Governance Groups and across the wider Programme

Programme (PMO)

0 mins – to be taken as read and discussed by exception

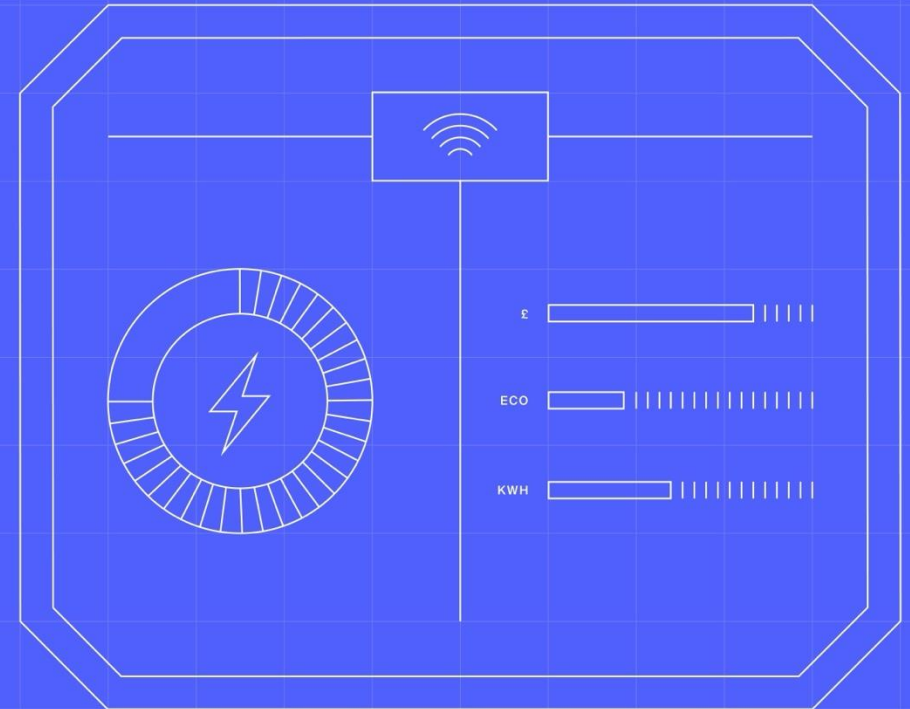

Governance group updates

Programme Steering Group (PSG)

PSG 04 June 2025

CR061 Decisoin: CR061 was approved by Ofgem

Readiness for Go-Live: Programme provided an update including Programme Status, a Critical Path POAP, Parties' Readiness Dashboard and a spotlight on M10 Acceptance Criteria and SIT Pathways to M10 Qualification.

Testing Update: Programme provided an update on SIT Functional, Migration which are now complete and on NFT and Ops testing.

Central Party Readiness for Go-Live: Helix provided an update on SAT, Service Management and their Readiness.

July M10 Checkpoint: An update was provided on the M10 Checkpoint in July

PSG papers available [here](#).

System Integration Testing Advisory Group (SITAG)*

SITAG 21 May 2025

SIT Exit Reporting Approach : SRO approved approved date changes to the following SIT milestones: T2-TE-0900, T2-TE-0950, T3-TE-0050, T2-TE-0850, T2-TE-0800

SIT Scope Modification Proposal: SRO approved the March SITF Scope Modification document

Data Working Group – Continuation: SRO approved the closure of the DWG from June onwards

Programme Milestones related to SITAG: SRO approved the proposed name changes which replace 'MVC' / 'Non-MVC' with 'SIT' and 'SIT Contingency' to the following SIT milestones: T3-TE-0046, T2-TE-0850, T3-TE-0043, T1-TE-2000, T3-TE-0052, T3-TE-0055, T3-TE-0051, T3-TE-0056, T3-TE-0059

SITAG papers available [here](#).

Design Advisory Group (DAG)

DAG 11 June 2025

Meeting held by correspondence owing to diminishing content.

Programme provided an update on IR8.11.

Programme provided an update on CR061 and CR062.

DAG papers available [here](#).

Qualification Advisory Group (QAG)*

QAG 22 May 2025

SIT / Non-SIT Qualification Pathways: SRO approved the renaming the following milestones: T3-QU-0085 - REC Code Manager / BSC PAB Approval of Qualification (MVC), T3-QU-0086 - REC Code Manager / BSC PAB Approval of Qualification (Non-MVC)

Non-SIT S&A QT Data Approach and Plan: SRO approved he Non-SIT S&A QT Data Approach and Plan v1.2

Non-SIT S&A QT Test Cases: SRO approved the Non-SIT S&A QT Test Cases (see headline report for full breakdown of documents)

Non-SIT LDSO QT Update: SRO approved the following milestones: T3-QU-0010 - Qualification Testing for Non-SIT LDSOs (Functional, Migration, NFT, Operational) 1 End, T3-QU-0079 -Non-SIT LDSOs submission deadline for their QT Test Completion Report to MHHS Programme

Sandbox Update: SRO approved the renaming of the following milestones: T3-QU-0126, T3-QU-0127 and SRO approved the addition of the following 2 new milestones: Sandbox Testing Start (UIT) - LDSO Participants, Sandbox Testing End (UIT) - LDSO Participants

QAG papers available [here](#)

Cross Code Advisory Group (CCAG)

CCAG 28 May 2025

In the meeting, the CCAG provided updates on:

Horizon Scanning Log: Updates from all Code Bodies on changes which may impact MHHS Programme.

Urgent/Fast Track Code Change Process: The Programme, BSC, REC provided an update on how Code Bodies can deliver urgent/fast track Code change. Will await input from DIP and SEC.

M8 Code Artefact Uplifts and CCAG Endorsement: Recommendation for M8 Code Artefacts Uplifts and Endorsement has been approved.

Reporting Milestones, CCAG Risks and Post-M6 Change: Programme provided an update on the milestone status, risks and Post M6/pre M8 Code Change Approach and Planning.

M8 Code implementation: Code Bodies and DIP Manager update on the M8 Code Implementation/go-live.

CCAG papers available [here](#).

Migration & Cutover Advisory Group (MCAG)*

MCAG 27 May 2025

Headline and Actions: DIP Manager to report progress on Offboarding Operational Process

Service Design Update (Elexon Helix): An update was given recent areas of consultation and areas of endorsements at the recent eTORWG and eSITAG meetings. Elexon Helix to confirm how and when ELS/Hypercare will be addressed.

M10 Readiness : Clarification was requested around SAT success criteria and implications for migration if delays persist. Concerns will be escalated to PSG.

Programme Milestones Related to MCAG: RED milestone T3-MI-0500 'M16 methodology approved' that this going to covered by the work stated by the Programme on the MWG updates.

MCAG papers available [here](#).

Wider Programme Updates

Participant Checklist:

There are a few updates this week, so this week's Participant Checklist includes the following items for Programme participant review, feedback and awareness:

- NEW! Systems Integration Testing (SIT) Functional and Migration Exit Reports - the deadline is **Tuesday 17 June 2025**
- NEW! Programme Participant Information Request (PPIR): Migration Contact Information for Central Parties – the deadline is **Thursday 19 June 2025**
- REMINDER: Migration Supplier Submission Round 2 – just over a week to go! The deadline is **Friday 20 June 2025**
- REMINDER: Design Interim Release 8.11 Artefacts published today!

You can view the **Participant Checklist** on the respective **Planning pages** of the [Collaboration Base](#) and the [MHHS website](#). In the Participant Checklist you can view upcoming consultations and key deliverables, as well as the latest status of Change Requests in the **Master Change Request Dashboard** tab.

We've created the **Interim Release and Swagger version alignment document** for SIT participants. You can view this document on the respective **SIT pages** of the [Collaboration Base](#) and [MHHS website](#).

Upcoming Governance Meetings:

- Thursday 12 June 2025:** Migration Working Group (MWG)
- Wednesday 18 June 2025:** Systems Integration Testing Advisory Group (SITAG)
- Thursday 19 June 2025:** Qualification Advisory Group (QAG)

*SITAG, MCAG, QAG replaced the Testing and Migration Advisory Group (TMAG) in Q1 2024.

Working Group Progress Report

Systems Integration and Testing Advisory Group (SITAG)*	
	Systems Integration Test Working Group (SITWG)
Upcoming deliverables	<ul style="list-style-type: none">SIT Operational Readiness ReportsSIT Regression Test Approach and Plan
Latest meeting's agenda items	03 July 2025 <ul style="list-style-type: none">TBC
Agenda items from last meeting	05 June 2025 <ul style="list-style-type: none">SIT Scope Modification ProposalSIT-A Settlement Testing progress ReportSIT Functional and Migration CompletionApproach to Service Management Re-TestingSIT Test Progress UpdateDefect Overview
L3 escalations	None

Qualification Advisory Group (QAG)*	
	Qualification and E2E Sandbox Working Group (QWG)
Upcoming deliverables	<ul style="list-style-type: none">N/A
Latest meeting's agenda items	08 July 2025 <ul style="list-style-type: none">TBC
Agenda items from last meeting	10 June 2025 <ul style="list-style-type: none">SIT & Non-SIT LDSO Qualification Pathways UpdateQualification Approach & PlanQAD Progress UpdateBSC Legacy AssuranceE2E Sandbox UpdateIF-47 in UIT GuidanceQualification Approach & Plan Annex 2QTC UpdatesWave 1 QT ReadinessWave 1 QT Checkpoint and QTC Set guidanceQualification Artefacts
L3 escalations	None

Working Group Progress Report


Migration and Cutover Advisory Group (MCAG)*			
	Migration Working Group (MWG)	Data Cleanse Working Group (DCWG)	Transition & Operational Readiness Working Group (TORWG)
Upcoming deliverables	<ul style="list-style-type: none"> N/A 	<ul style="list-style-type: none"> N/A 	<ul style="list-style-type: none"> N/A
Latest meeting's agenda items	3 July 2025 <ul style="list-style-type: none"> MWG Update MWG Backlog 	26 June 2025 <ul style="list-style-type: none"> Upcoming Data Cleanse Activities Domestic Premises Indicator Data Inconsistencies ESME ID Exception Resolution Meter Location and Number of Displayed Register Digits Exception Resolution Data Cleanse Reporting Data Cleanse Handover Related MPANs 	11 June 2025 <ul style="list-style-type: none"> M10/M11 Participant Cutover Plans Qualification Pathways Updating ISD at M10 Service Design Update
Agenda items from last meeting	12 June 2025 <ul style="list-style-type: none"> MWG Update MWG Backlog 	29 May 2025 <ul style="list-style-type: none"> Upcoming Data Cleanse Activities Domestic Premises Indicator Data Inconsistencies ESME ID Exception Resolution Meter Location and Number of Displayed Register Digits Exception Resolution Data Cleanse Reporting 	14 May 2025 <ul style="list-style-type: none"> M10/M11 Participant Cutover Plans Timings for Participants Qualification Updating ISD at M10 Update on discussions to de-link DIP onboarding and qualification for LDSOs Outputs from request run through sessions Service Design Update Codification of Service Management
L3 escalations	None	None	None

Summary and Next Steps

INFORMATION: Summarise actions/decisions and future MCAG and working group meetings

Chair & Secretariat

5 mins

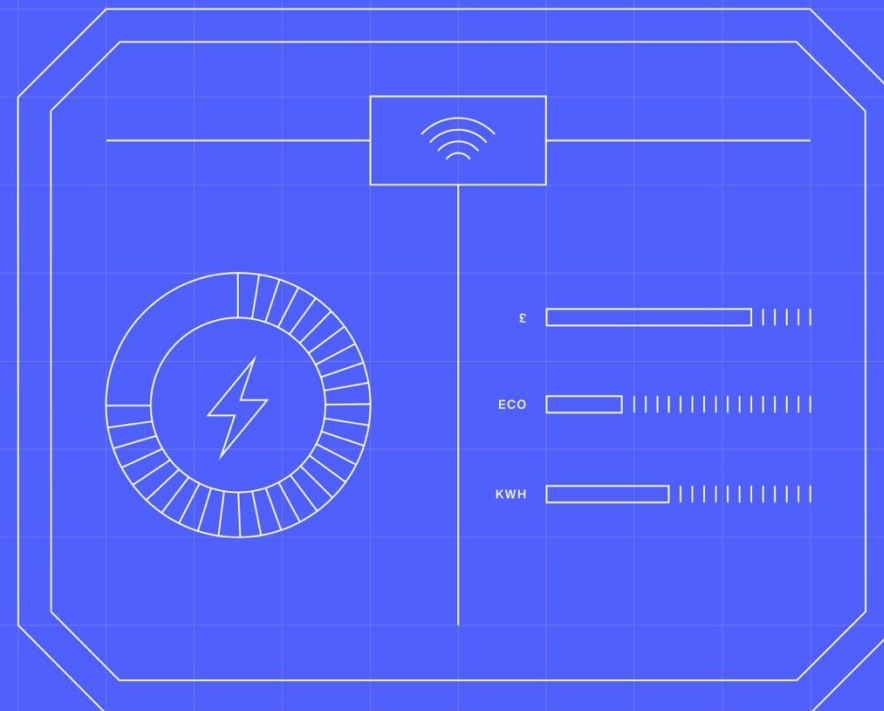

Summary and Next Steps

Next steps:

- 1. Confirm actions and decisions from meeting
- 2. Date of next MCAG: **Tuesday 24 July 2025 at 2pm**
- 3. Dates of next working groups:
 - Date of next MWG: **3 July 2025**
 - Date of next DCWG: **8 July 2025**
 - Date of next TORWG: **9 July 2025**

Upcoming agenda items:

Meeting dates		24 August 2025
Relevant milestones or activities	<ul style="list-style-type: none">• M10 Checkpoint Update	
Agenda items	<ul style="list-style-type: none">• Service Design Update - Elexon• MWG Update• DCWG Updates• TORWG Updates	
Standing items	<ul style="list-style-type: none">• Headline Report and Actions• Programme Milestones related to MCAG• Top Programme Risks related to MCAG• Programme Updates• Summary and Next Steps	

If you would like to propose an agenda item for the MCAG, please contact the PMO@mhhsprogramme.co.uk
